

Project update

April 2023

Upcoming work at Martin Place metro station

Martin Place Station site

- Finishes will continue to be the focus of the north shaft of the station in the month of April.
- Ceiling GRC (glass reinforced concrete) installation will continue throughout the station including the walls and ceilings.
- Installation of the elevator in the northern atrium will be completed in April. This elevator will take commuters from the platform level to the retail level of B3.
- The platforms continue to evolve with aluminium installation to finish the ceilings progressing.
- The south shaft of the station has progressed with 90% of the structure now complete. The last portion of the structure will be completed late April.
- The temporary upper deck of the southern atrium will be removed in April, which will open up the space between tower and station.
- Services installation will continue in both the north and south shafts throughout April.

Martin Place North site

- The structure will continue to climb in April and expected to reach level 36. The concrete slabs are noticeably smaller with the curve of the building obvious from street level.
- Fit-out activities are progressing throughout the building including ceiling and underfloor services.
- Steel installation in the western atrium will reach level 23 with the façade reaching level 18 in April.
- Façade installation on the overall building structure will continue with the target of installing up to level 22 by end of April.

Martin Place South site




























- During April, the structure will reach level 11. The concrete slabs have now reduced in size and form part of the high rise portion of the building.
- High level services installation on the lower floors are progressing.
- Installation of the first façade panels will commence in April, marking a significant milestone for the project.
- Escalators to the tower lobby are also planned for installation in April.

General work activities

- Plant and equipment, machinery and materials will be delivered and removed from the Martin Place North and South sites.
- Fit-out work inside the tunnels by Systems Connect will continue to take place **24 hours a day, seven days a week**.
- **From Friday 17 March 2023**, JCG, the tunnelling contractor for **Sydney Metro West Hunter Street Station**, will occupy the existing Sydney Metro Bligh Street site including the construction offices and acoustic shed. Deliveries via O'Connell Street for Sydney Metro Martin Place have ceased from this date.

What to expect

- Some activities will be noisy. The project team will limit these impacts wherever possible.
- Equipment used will include excavators, road header, jackhammers, concrete pumps, concrete and haulage trucks, cranes, bobcats, forklifts, elevated work platforms, vacuum trucks, street sweepers, saw cutters and hand tools.
- Non-tonal reversing beepers will be used, and workers will be instructed to keep noise to a minimum.
- Temporary traffic changes including shoulder and parking lane closures and short-term traffic lane closures may be required.
- Access to buildings and driveways will be maintained at all times.
- Pedestrian footpaths may be closed or narrowed for short periods with diversions in place.
- There will be increased light vehicle and truck movements in and out of sites.
- Traffic control and directional signage will be in place for the safety of workers and the community.
- Temporary lighting towers required during night work will be directed away from properties where possible.

Activity (subject to change)	March 2023	April 2023	May 2023
Temporary pedestrian changes and diversions			
Delivering and removing materials, machinery, spoil, and equipment			
Concrete pours including formwork and reinforcement installation			
Crane use			
Driveway and parking zone changes			
Utility work and geotechnical investigations			
Survey monitoring			
Steel structure installation			
Services and fit-out work			

 **1800 171 386** Community information line open 24 hours

 **martinplacemetro@transport.nsw.gov.au**

 Sydney Metro City & Southwest, PO Box K659, Haymarket NSW 1240

 If you need an interpreter, contact TIS National on **131 450** and ask them to call **1800 171 386**

Work hours

Standard work hours are Monday to Friday, 7am to 6pm and Saturday, 8am to 6pm. Following consultation, additional work hours have been approved to take advantage of times when traffic and pedestrian volumes are lower. **Extended work hours at the Martin Place North and South sites are Monday to Saturday, 5am to 10pm and Sunday, 7am to 6pm.**


Location	Work during standard (extended) hours	
Martin Place South site	<ul style="list-style-type: none"> General construction Delivering and removing equipment, machinery, spoil and materials Core wall and suspended slab construction Dewatering and ventilation 	<ul style="list-style-type: none"> Escalator installation Concrete pouring of building basement structure Installing perimeter formwork screens Builder's work, services and fit-out work
Martin Place North site	<ul style="list-style-type: none"> General construction Delivering and removing equipment, machinery, spoil and materials Core wall and suspended slab construction Escalator and lift installation 	<ul style="list-style-type: none"> Dewatering and ventilation Installing perimeter formwork screens Installation of structural steel for western atrium Builder's work, services and fit-out work
Location	Out-of-hours work	
Martin Place South site	<ul style="list-style-type: none"> Delivering and removing equipment, machinery, and materials Dewatering and ventilation 	<ul style="list-style-type: none"> Utility work and investigations Delivering and pumping concrete
Martin Place North site	<ul style="list-style-type: none"> Delivering and removing equipment, machinery, and materials Dewatering and ventilation 	<ul style="list-style-type: none"> Hoarding modification work Utility work and investigations Delivering and pumping concrete

 **1800 171 386** Community information line open 24 hours

 **martinplacemetro@transport.nsw.gov.au**

 Sydney Metro City & Southwest, PO Box K659, Haymarket NSW 1240

 If you need an interpreter, contact TIS National on **131 450** and ask them to call **1800 171 386**

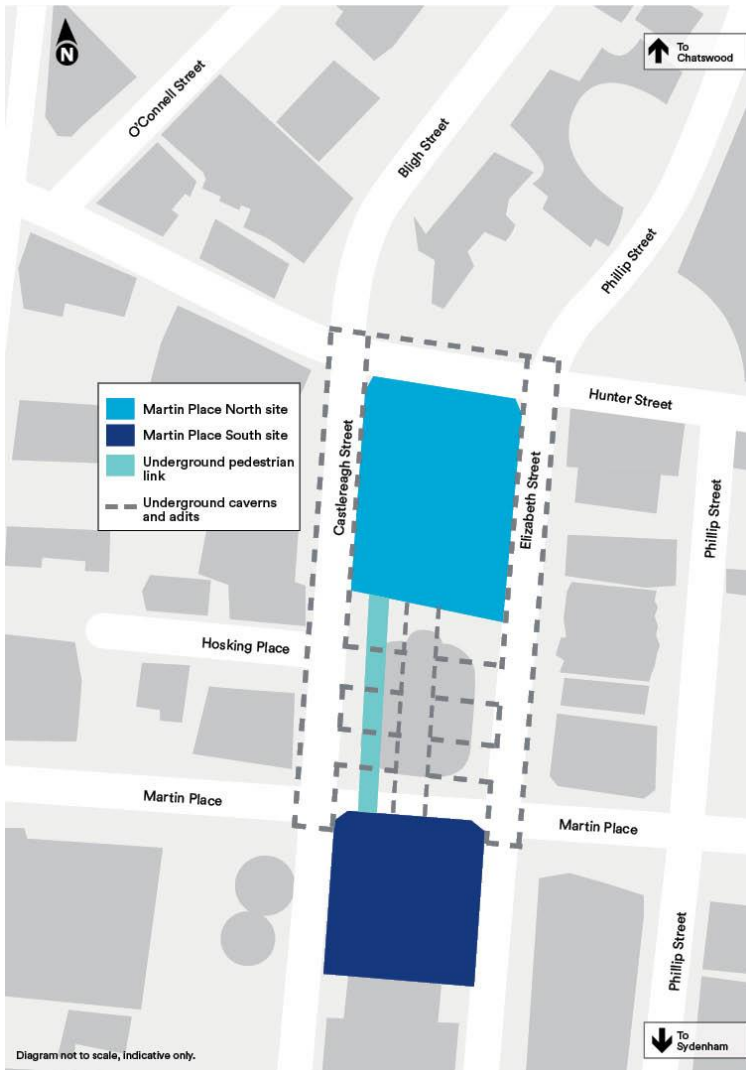

Martin Place metro station sites

Thank you for your cooperation and understanding while we complete this essential work.

If you have any questions about the Martin Place integrated station development, please contact the community team on **1800 171 386** (24-hour community information line) or email

martinplacemetro@transport.nsw.gov.au

For questions about the tunnel fit-out work, please contact Hubavina on **1800 171 386** or email

linewidemetrol@transport.nsw.gov.au

For any questions about the tunnelling works at the Bligh Street site for Sydney Metro West Hunter Street project, please contact Shay from the JCG community team on **1800 612 173** or email

MetroTunnelsJCGJV@transport.nsw.gov.au

 **1800 171 386** Community information line open 24 hours

 martinplacemetro@transport.nsw.gov.au

 Sydney Metro City & Southwest, PO Box K659, Haymarket NSW 1240

 If you need an interpreter, contact TIS National on **131 450** and ask them to call **1800 171 386**
