



HBI

Healthy Buildings International Pty Ltd

A.C.N. 003 270 693

A.B.N. 39 003 270 693

Suite 2.06, Level 2
29-31 Solent Circuit
Norwest, NSW 2153

Tel: 61 (02) 9659 5433
e-mail: hbi@hbi.com.au
Web: www.hbi.com.au

6 March 2026

Ref: 170108-ER_DPHI Feb 2026

[REDACTED]
Team Leader Compliance – Government Projects
Department of Planning, Housing and Infrastructure
Locked Bag 5022
PARRAMATTA NSW 2124

Dear [REDACTED]

RE: Sydney Metro City and South West – ER Monthly Reports for February 2026

Healthy Buildings International (HBI) submits this report to the Secretary in accordance with:

- Condition A26 (j) of the Sydney Metro Sydenham to Bankstown Upgrade SSI_8256 Approval (12 December 2018) and associated modifications MOD1_Bankstown Station and Mod 2_Modification to A9, D3 and E53 (2 June 2025).

The attached summaries detail the key activities undertaken by Environmental Representatives for Sydney Metro – City and Southwest, Sydenham to Bankstown for the month of **February 2026**.

Note that this report is separate to the proposed final Environmental Representative Report required to be submitted to the Secretary for the Sydney Metro – City and Southwest, Chatswood to Sydenham for the period of 1 January 2026 to 31 December 2026 to be submitted by 29 January 2027.

Yours sincerely

[REDACTED]
Environmental Representative

Cc: Sydney Metro [REDACTED]

AA: Available on Sydney Metro Website

Contractors: Available to Contractors on Sydney Metro Website

DPHI Compliance: Portal

DPHI Post Approvals: Available on Sydney Metro Website



Table of Contents

1.	Sydenham to Bankstown – TSOM.....	3
2.	Southwest Metro Corridor Package 3 (SWM3) JHLOR.....	4
3.	Errant and Hostile Vehicle Mitigation Treatments (EHVMT)	8
4.	Sydney Metro Retained Obligations (SM).....	10
5.	Statement of Limitations	11



1. [Sydenham to Bankstown – TSOM](#)

Project Approval	Contract Package	EPL	Environmental Representative/s
SSI 8256 (S2B)	Trains, Systems, Operation and Maintenance (TSOM)	JHLOR EPL 21147 – MTR continues to work under JHLOR CEMP, and subplans SSI 8256	[REDACTED]
Key Construction Activities During the Period			
<ul style="list-style-type: none"> ▪ Southwest corridor and stations <ul style="list-style-type: none"> • Testing and commissioning of electrical infrastructure • High Speed testing and commissioning of trains • Testing and commissioning of Public Announcement (PA) Systems, Closed Circuit Television (CCTV) Cameras at platforms 			
Key Construction Activities Look Ahead			
<ul style="list-style-type: none"> ▪ Southwest corridor and stations Marrickville, Dulwich Hill, Hurlstone Park, Canterbury, Campsie, Belmore, Lakemba, Wiley Park, Punchbowl and Bankstown Stations: <ul style="list-style-type: none"> • Testing and commissioning of field equipment • Dynamic Train Testing activities 			
ER Inspections			
<ul style="list-style-type: none"> ▪ The works at station platform and Metro Service Buildings (MSBs) such as cable pulling were observed by the ER while inspecting SWM3 sites, no issues were raised. 			
Photos			
<ul style="list-style-type: none"> ▪ N/A 			
Endorsed Document/s			
<ul style="list-style-type: none"> ▪ There were no endorsed documents this month. 			
Community Consultation			
The monthly project related notifications were issued on 20 February 2026.			
Non-compliance/ Incidents or Repeat Complaints			
<p>Sydney Metro has been providing summaries of complaints to DPHI weekly and a summary to the ER. Responses to each complaint have been noted in each complaint report, with follow up actions often defined in revised reports. Key or repeat items of note are discussed below for the respective projects.</p> <p>There were no incidents for TSOM reported to the ER under condition A36 of SSI 8256.</p> <p>No non-compliances were raised by the ER, Sydney Metro or reported to the ER during the reporting period.</p> <p>Project related complaints:</p> <ul style="list-style-type: none"> ▪ No complaints were received during the reporting period (down to zero from three in the previous month). <p>Unrelated Project complaints:</p> <ul style="list-style-type: none"> ▪ No unrelated project complaints were received during the reporting period. 			
Audits			
<ul style="list-style-type: none"> ▪ No audits were undertaken during this reporting period. 			
Looking Forward – Core Focus Areas			
<ul style="list-style-type: none"> ▪ Works at platforms within close proximity of heritage listed stations ▪ Testing and commissioning (Trial Running activities) between Sydenham and Bankstown 			



2. [Southwest Metro Corridor Package 3 \(SWM3\) JHLOR](#)

Project Approval	Contract Package	EPL	Environmental Representative/s
SSI 8256 (S2B)	Southwest Metro Corridor Package 3 (SWM3) JHLOR	#21147	[REDACTED]
Key Construction Activities - During the Period			
<p>General:</p> <ul style="list-style-type: none"> ▪ Minor works for various disciplines including security gates, earthing and bonding electrical works ongoing ▪ Completion of bridge screens installation at Foord Avenue, Hurlstone Park, Ness St and Cooks River ▪ Dulwich Hill Station - Plaza and retaining wall installation complete, area opened to the public ▪ Foord Avenue, Hurlstone Park - Overhead Crash Beam installation works complete ▪ Ness Street, Dulwich Hill - Overhead Crash Beam installation works nearing completion ▪ Security fence repairs nearing completion ▪ Planning underway for pedestrian and cyclist bridge within rail corridor near Ness Street, Dulwich Hill ▪ Bedford Crescent, Dulwich Hill – pavement and landscaping works complete <p>All Corridor Stations (summary):</p> <ul style="list-style-type: none"> ▪ Services install. Gutter/down pipe installation, UGL wiring & testing of platform doors, internal fit out and painting ▪ Installation of brackets and containment continues. Roofing and painting works nearing completion <p>Other works:</p> <ul style="list-style-type: none"> ▪ Canterbury Compound - Site offices and amenities in operation, ongoing fuel and gas storage ▪ North Terrace Compound, Bankstown: Site offices and amenities, ongoing fuel and gas storage ▪ Belmore Triangle - Laydown area operations ongoing including material stockpiles, concrete and liquid waste management ▪ Punchbowl Station - Platform works nearing completion, landscaping works and retaining wall works ongoing ▪ Campsie - Platform works nearing completion ▪ Marrickville Station - Platform works nearing completion ▪ Canterbury Station – Platform works nearing completion ▪ Lakemba Station – Platform and landscaping works nearing completion ▪ Belmore Station – Platform works ongoing ▪ Wiley Park - Platform works ongoing ▪ Bankstown Station – Platform works nearing completion ▪ Ongoing tree impact assessments related to Corridor Intrusion Detection Systems and Object Detection Systems (CIDS/ODS), pruning, removal and ecologist supervision. Some sections adjacent to Threatened Ecological Communities (TECs) and threatened species, e.g. Belmore Station, Bruerst Street ramp (Punchbowl), Urunga Parade (Punchbowl), South Terrace (Bankstown) ▪ Ongoing installation of security cameras related to CIDS/ODS package ▪ Vegetation and weed management within the rail corridor ▪ Stockpile management including waste classification, waste tracking, load-in / load-out, management of site accesses and truck routes 			



Key Construction Activities Look Ahead	
<ul style="list-style-type: none">▪ Platform works at all stations▪ Charles Street Overhead Crash Beam installation▪ Survey and defect inspections at all stations▪ Vegetation removal related to JHLOR and CIDS and ODS packages▪ Installation of security cameras at various locations within the rail corridor▪ Testing and commissioning between Sydenham and Bankstown	
ER Inspections	
<p>ER inspections are now conducted monthly based on the risk profile. One ER inspection was conducted in the reporting period on 18 February 2026. Minor issue related to graffiti on shade cloth at Dulwich Hill Station Plaza worksite and Campsie were raised during this inspection which were promptly resolved by the contractor.</p>	
Photos	
	
<p>Figure 1 – Dulwich Hill Plaza works completed, area opened to the public.</p>	<p>Figure 2 – Bedford Crescent, Dulwich Hill – Landscaping and pavement works completed, area opened to the public.</p>
	
<p>Figure 3 – Ness Street, Dulwich Hill – Overhead Crash Beam installation works completed.</p>	<p>Figure 4 – Foord Avenue, Hurlstone Park – Overhead Crash Beam installation and bridge screen installation works completed.</p>

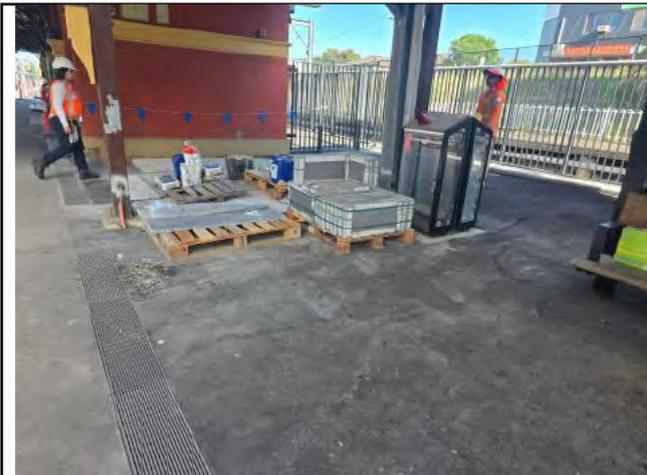


Figure 5 – Campsie Station – Ongoing platform tiling works.



Figure 6 – Campsie Station - Cable installation within cable trays ongoing.



Figure 7 – Belmore Triangle - Ongoing imported material stockpile and waste stockpile management.



Figure 8 – Bankstown - Plaza works ongoing including tiling, landscaping and finishing works.

Endorsed Document/s

- There were no endorsed documents this month.

Community Consultation

The monthly project related notifications for February 2026 were issued in late January 2026 and further updates for February 2026 were provided on 25 February 2026. Project specific consultation was undertaken with the affected communities regarding out-of-hours works between 15 February and 25 February 2026.

Non-compliance/ Incidents or Repeat Complaints

Summaries of CSW complaints are now received on a weekly basis. Complaints are discussed where relevant below.

No NCRs were raised by the ER or Sydney Metro or reported to ER and SM by JHLOR:

There were no incidents reported to the ER under Condition A36 of SSI 8256.

No Class 3 environmental incidents related to JHLOR were reported.

The ER is aware of the following complaints related to SWM3 package. The number of complaints increased in comparison to the previous month continuing work at all locations.

- One complaint related to worker behaviour at Hurlstone Park Station



- One complaint related to Property Damage/Prevention at Hurlstone Park
- One complaint related to Traffic, Transport and Parking at Canterbury

Unrelated SWM3 Project complaints:

- No unrelated project complaints were received during the reporting period.

Audits

No audits were undertaken during this reporting period.

Summary of Environmental Performance

Environmental risks are generally associated with out of hours works during possessions and maintaining compliance with the Tree Report during the security fence installation. Actions raised during ER inspections are closed out within the agreed timeframe with useful supporting documentary evidence provided.

Looking Forward – Core Focus Areas

- Platform works and heritage management
- Overhead Crash Beam installation at Charles St, Canterbury adjacent to VIVA fuel pipeline and heritage listed bridge wingwall
- Management of noise and vibration during out-of-hours work during possessions
- Respite offers related to OOHW at various locations
- Management of tree impacts, Plant Community Types (PCTs) and Threatened Environmental Communities (TECs) during construction of security fencing along the alignment, and maintenance of the buffer zone.



3. [Errant and Hostile Vehicle Mitigation Treatments \(EHVMT\)](#)

Project Approval	Contract Package	EPL	Environmental Representative/s
SSI 8256 (S2B)	Errant and Hostile Vehicle Mitigation Treatments (EHVMT) Martinus Rail	No EPL	[REDACTED]
Key Construction Activities - During the Period			
<p>Construction Activities:</p> <p>General:</p> <p>Minor Ancillary Facilities operating at Belmore. North Terrace/Stacey Street, Bankstown Minor Ancillary Facility has been demobilised.</p> <ul style="list-style-type: none"> • Canterbury Road – Utility relocation works complete, piling works commenced on westbound lane • Stacey Street – Footpath and concrete barrier work completed with handrail installation works remaining to be completed in the coming months. <p>Completed sites:</p> <ul style="list-style-type: none"> • Loch Street • Burwood Road • Moreton Street • Haldon Street • King Georges Road • Punchbowl Road • Livingstone Road • Wardell Road • Duntroon Street • Melford Street • Illawarra Road • Garnett Street • Albermarle Street • Wattle Street/North Terrace • Bruest Place/Kelly Street Punchbowl • Peel St • Railway Pde • Dennis St • Railway Pde • Kier Avenue/Hurlstone Park • Dudley Street 			
Key Construction Activities Look Ahead			
<ul style="list-style-type: none"> ▪ Stacey St, Bankstown – Handrail installation works ▪ Canterbury Road, Canterbury – Sydney Water main relocation works 			
ER Inspections			
<ul style="list-style-type: none"> ▪ ER inspections are undertaken based on scope/risk levels of the activities. No ER Inspection was undertaken in February 2026 due to majority of the works completed. 			



Photos
No ER inspections were undertaken in the reporting period.
Endorsed Document/s
ER reviewed the following documents and provided comments to the contractor to update: <ul style="list-style-type: none">25/02/2026 – OOHW#26 – Rev A – ER endorsement of OOHW planned in March 2026 related to Sydney Water asset. Works are required to be undertaken at night due to road occupancy licence restrictions and include removal of temporary water main provisions, completion of the new City-Side concrete footpath. Contractor has planned noise intensive activities (saw cutting) to be completed prior to midnight with road occupancy licence commencement from 9pm. One recommendation for alternative accommodation and four recommendations of respite offers were provided to the affected residents.23/02/2026 – SWM4 – Q1Q2 2025 CTR – Final revision12/02/2026 – Minor Ancillary Facility Checklist – Close St, Canterbury – Rev A
Community Consultation
The February Monthly Update notifications were issued in late January 2026, and project specific consultation was undertaken with the affected communities regarding out-of-hours works in late January 2026.
Non-compliance/ Incidents or Repeat Complaints
Since commencement of City metro services passenger operations on Monday 19 August 2024, Sydney Metro is now providing summaries of CSW complaints on a weekly basis (was provided daily until 16 August 2024) to DPHI and ERs covering complaints related to remaining construction works.
There were no non-compliances raised by the ER or reported to the ER during the reporting period. There were no incidents reported to the ER under Condition A36 of SSI 8256. There were no Class 3 environmental incidents reported to the ER during the reporting period.
ER is aware of the following complaints received during the reporting period. The number of complaints increased in comparison to the previous reporting period (two to five) due to the increased OOH activities: <ul style="list-style-type: none">Two complaints related to traffic transport and parking at Canterbury and BankstownOne complaint related OOHW notifications at CanterburyTwo complaints related to OOHW related Noise and Vibration
Unrelated SWM4 Project complaints: <ul style="list-style-type: none">No unrelated project complaints were received during the reporting period.
Audits
No audits were undertaken during this reporting period.
Looking Forward – Core Focus Areas
<ul style="list-style-type: none">Sydney Water Asset relocation at CanterburyManagement of noise and dust during out-of-hours worksCompliance reporting and completion of conditions and recommended environmental mitigation measures



4. [Sydney Metro Retained Obligations \(SM\)](#)

Project Approval	Contract Package	EPL	Environmental Representative/s
SSI 8256 (S2B)	Sydney Metro Retained Obligations (SM)	Not applicable	[REDACTED]
Key Construction and other Activities			
Ongoing works related to dynamic testing related activities for Southwest including variable speed testing of the metro trains			
ER Inspections			
ER Inspections are undertaken on a scope/risk level of activities. There were no inspections undertaken related to City section as Chatswood Remediation site and Mowbray Road Shared Path works have been completed.			
Endorsed Document/s			
<ul style="list-style-type: none"> ▪ No endorsed documents in this period. ▪ Discussions are ongoing with DPHI regarding Environmental Representative review of a proposed Minor Works Application related to Trial Running activities. 			
Non-compliance/ Incidents or Repeat Complaints			
<p>Since commencement of First Passenger Service on the City portion of CSW, Sydney Metro now provides summaries of CSW complaints on a weekly basis to DPHI and ERs covering complaints related to remaining construction works. Key or repeat items of note are discussed below for the respective projects, where applicable or under respective CSW packages.</p> <p>No complaints were reported to the ER during the reporting period. No incidents were reported to the ER during the reporting period. No non-compliances were raised by the ER/SM or reported to the ER during the reporting period.</p>			
Audits			
No audits were undertaken during this reporting period.			
Looking Forward – Core Focus Areas			
<ul style="list-style-type: none"> ▪ CTRs for Q3Q4 2025 for SSI7400 and SSI8256 SMRO sections ▪ Testing and Commissioning between Sydenham and Bankstown ▪ Collaborating with MTR and MTS to ensure the required documents are ready for the First Passenger Service. 			



5. [Statement of Limitations](#)

Healthy Buildings International (HBI) has prepared this report in accordance with the requirements of Condition A24(l) of the Sydney Metro Condition A26(j) of the Sydney Metro Conditions of Approval (CSSI 17_8256).

The report is for the sole purposes of Department of Planning, Housing and Infrastructure (DPHI) and Sydney Metro. It has been prepared based on generally accepted practices and standards at the time it was prepared. No other warranty, expressed or implied, is made as to the professional advice included in this Report. This report did not assess any aspects relating to safety.

Where the Report indicates that information has been provided to HBI by third parties, HBI assumes no liability for any inaccuracies in or omissions to that information.

This Report was prepared based on the conditions encountered and information reviewed for the period of reporting. HBI disclaims responsibility for any changes that may have occurred after this time.

This Report should be read in full. No responsibility is accepted for use of any part of this report in any other context or for any other purpose or by third parties. This Report does not purport to give legal advice. Legal advice can only be given by qualified legal practitioners.

Except as required by law, no third party may use or rely on this Report unless otherwise agreed by HBI in writing. Except as specifically stated in this section, HBI does not authorise the use or findings of this Report by any third party.

To the extent permitted by law, HBI expressly disclaims and excludes liability for any loss, damage, cost or expenses suffered by any third party relating to or resulting from the use of, or reliance on, any information contained in this Report. HBI does not admit that any action, liability, or claim may exist or be available to any third party.
