

## Notification – Campsie

Planned Rail Shutdown - July 2022

**The T3 Bankstown Line between Sydenham and Birrong will be closed between Saturday 2 July and Friday 15 July 2022 for metro upgrade work.**

Opal enabled rail replacement bus services will be available during this time. You can plan your trip at [transport.nsw.info](http://transport.nsw.info) and on real time apps from late June. Kerbside changes will also be in place around affected train stations for temporary bus zones. Please check signage before parking your car.

**To maximise the amount of work that can be done when trains are not running, work on the new Metro line will take place continuously throughout the shutdown period from 2am Saturday 2 July to 2am Saturday 16 July.**

### Important information about planned work during the upcoming rail shutdown

As a result of ongoing industrial action at Sydney Trains since late 2021, a range of planned activities along the Bankstown Line have been postponed until power isolations are available again. Many of these postponed activities are scheduled to take place during the upcoming rail shutdown in the July school holidays.

Most of the work to upgrade the Bankstown Line to Sydney Metro standards requires power isolations to ensure workers can safely complete works. This includes any work near live electrical feeders, cable installation, power works, lift and staircase installation, as well as canopy and bridge upgrade works. The work detailed in this notification is subject to the same requirements and may be impacted by future industrial action.

This is outside of Sydney Metro's control. We appreciate your patience and apologise for any delays. We will continue to notify properties close to our work sites about activities that will impact them directly.

Location	Details of work during the planned shutdown - from 2am Saturday 2 July until 2am Saturday 16 July
Campsie (along the rail corridor)	<ul style="list-style-type: none"> <li>• Installation of high voltage cables from South Parade to Lilian Street from 6am 5 July to 7am 13 July</li> <li>• Investigation of existing/new services for excavations and penetrations</li> <li>• Construction of combined service route</li> <li>• Construction of segregation fence footings, trackside equipment footings and local services routes</li> <li>• Installation of fencing including segregation fencing along the corridor and station precincts, cable service routes, galvanised steel troughing (GST)</li> <li>• Modification and upgrade work to bridges along Wairoa Street including changes to traffic conditions:</li> <li>• Temporary lane closures continue along Wairoa Street between South and East Parade for a period of four (4) weeks</li> <li>• Installation of signal equipment including cable pulling</li> <li>• Refurbishment activities to over-wiring structures including removal of redundant footings and structures</li> <li>• Modification to bridges along the alignment along Duke Street footbridge and Loch Street Bridge</li> <li>• Temporary traffic changes include:               <ul style="list-style-type: none"> <li>• Temporary closure of Loch Street Bridge. Traffic diversions will be in place via Ninth Avenue, Beamish Street and Evaline Street</li> <li>• Temporary closure of Duke Street footbridge. Pedestrian diversions will be in place via Beamish Street</li> </ul> </li> </ul>
Around Campsie Station	<ul style="list-style-type: none"> <li>• Pedestrian detour on Beamish Street between North and South Parade for crane and concrete pump operation</li> <li>• New structural steel canopy and roof structure</li> <li>• Building and fitout works on concourse building and station platform buildings</li> <li>• Installing footings for furniture, fencing and equipment on station platform buildings</li> <li>• Remediation of building façade, and installation of new building facade mesh screens</li> <li>• Block work on platform walls</li> <li>• Installing structural steel, block, brick and roofing work at the new services building and concourse buildings</li> <li>• Refurbishing platform stairs, ceilings and lights, and platform 2 brick veneer retaining wall construction</li> <li>• Building fitout to concourse and station buildings including mechanical, electrical, plumbing work</li> <li>• Track side equipment footing install</li> <li>• Installing fencing along Beamish Street, Platform 2 and Platform 0</li> </ul>


	<ul style="list-style-type: none"> <li>Mechanical, electrical and plumbing cable containment to concourse and station buildings</li> </ul>
Services building site at Lilian Lane opposite Dewar Street	<ul style="list-style-type: none"> <li>Installation of new high voltage pole and relocating existing aerial wires</li> <li>Installation of new structural steel on metro service building</li> <li>Construction of trackside equipment footings and local services routes</li> </ul>
Substation site (Off Lilian Street)	<ul style="list-style-type: none"> <li>Installing conduits, facade walls and panels</li> <li>Traffic controllers to facilitate truck movements on Lilian Street</li> <li>Bulk power supply installation into the traction substation</li> <li>Installing perimeter columns and steel screens, cables and cable supports</li> <li>Building the driveway to roads standards, and landscaping and street works</li> <li>Mechanical and electrical fit out</li> </ul>

### Planned work during the remainder of July (16 July to 30 July)

Following the planned shutdown, between **Saturday 16 July and Saturday 30 July**, work will continue during standard construction hours, **Monday to Friday 7am to 6pm and Saturday 8am to 6pm**. All work activities are subject to relevant approvals and will be tailored to the evolving Covid-19 situation. Due to the nature of some activities and for the safety of workers, some work will also be completed outside of standard hours, including at night. Planned out-of-hours work following the shutdown are detailed in the table below.

Date / time	Details of planned work 16-30 July
Standard construction hours between <b>Saturday 16 July and Saturday 30 July</b>	<ul style="list-style-type: none"> <li>Work at the substation site detailed in the above table will continue for the remainder of July in standard construction hours.</li> <li>Site investigations and surveys, delivery of construction plant and material and associated activities</li> <li>Concrete work associated with installing new cable routes and bridge upgrades.</li> <li>Installation of fencing, cable service routes and galvanised steel troughing (GST)</li> <li>Modification and upgrade work to bridges along Wairoa Street including changes to traffic conditions: <ul style="list-style-type: none"> <li>Temporary lane closures continue along Wairoa Street between South and East Parade for a period of four (4) weeks</li> </ul> </li> </ul>
Mid-week between <b>6pm and 7am Saturday 16 July to Saturday 30 July</b> (for no more than 3 nights per week)  Access to buildings and driveways will be maintained at all times.	<ul style="list-style-type: none"> <li>Various site investigations and surveys including but not limited to non-destructive digging, soil assessments, geotechnical investigations and surveys for drainage, utilities, and fencing</li> <li>Removal of trees and vegetation throughout the rail corridor where required</li> <li>Installation of fencing, cable service routes and galvanised steel troughing</li> <li>Delivery of plant and material including preparatory activities for upcoming out-of-hours work</li> <li>Installation of signal equipment including cable pulling</li> <li>Delivery of plant and material including preparatory activities for upcoming out-of-hours work</li> <li>Refurbishment activities to over-wiring structures including removal of redundant footings and structures</li> <li>Concrete works associated with installing galvanised steel troughing, new cable routes and bridge upgrades</li> </ul>

Equipment used for the above work will include a range of heavy machinery and hand and power tools. Properties close to scheduled work will receive notifications when construction work is scheduled to occur. You can contact us on **1800 171 386** (24 hour community information line). If you have questions about the **substations** please ask for **Chris** or email [LinewideMetro@transport.nsw.gov.au](mailto:LinewideMetro@transport.nsw.gov.au). For all other works please ask for **Claire** or email [SouthwestMetro@transport.nsw.gov.au](mailto:SouthwestMetro@transport.nsw.gov.au).  
**Thank you for your cooperation while we complete this essential work.**

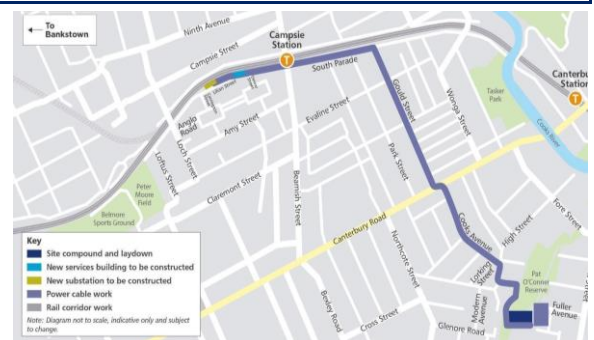

 **1800 171 386** Community information line open 24 hours

 [southwestmetro@transport.nsw.gov.au](mailto:southwestmetro@transport.nsw.gov.au)

 Sydney Metro City & Southwest, PO Box K659, Haymarket NSW 1240

 If you need an interpreter, contact TIS National on **131 450** and ask them to call **1800 171 386**
